Drylaw Shopping Centre

City of Edinburgh Council

LUDDON CONSTRUCTION LIMITED
Balmore House, 1497 Balmore Road
Glasgow G23 5HD
Tel: 0141 945 2233

ID	Name	Planned Duration	Time Risk Allowance	Planned + TRA Duration	Total Float	Start	Finish
B62981	**Drylaw Shopping Centre**	**0d**	**0d**	**0**	**78d**	**04 May 26**	**21 Aug 26**
1	**Contract Award**	**0d**	**0d**	**0**	**0d**	**05 May 26**	**05 May 26**
2	**Start Date**	**0d**	**0d**	**0**	**1d**	**04 May 26**	**04 May 26**
3	**Site Set Up**	**0d**	**0d**	**0**	**1d**	**05 May 26**	**05 May 26**
4	Erect Compound	0d	0d	0	1d	05 May 26	05 May 26
5	Take Delivery of Plant	0d	0d	0	1d	05 May 26	05 May 26
6	Cat Scan Work Site	0d	0d	0	1d	05 May 26	05 May 26
7	Setting Out	0d	0d	0	1d	05 May 26	05 May 26
8	**Phase 1**	**0d**	**0d**	**0**	**18d**	**05 May 26**	**28 May 26**
9	Traffic Management	0d	0d	0	0d	05 May 26	05 May 26
10	Road Closure - PH1	0d	0d	0	0d	05 May 26	05 May 26
11	Slabbed Area	0d	0d	0	18d	05 May 26	28 May 26
12	Downtakings	0d	0d	0	2d	05 May 26	06 May 26
13	Excavate Existing Footway - 13.5m2	0.3d	0.7d	1	1d	05 May 26	05 May 26
14	Excavate Existing Carriageway - 42.5m2	0.5d	0.5d	1	1d	06 May 26	06 May 26
15	Removal of Kerb 15m	0.2d	0.8d	1	1d	05 May 26	05 May 26
16	Drainage	0d	0d	0	1d	07 May 26	07 May 26
17	Install Gully Pot & Cover - 1Nr	0.3d	0.7d	1	1d	07 May 26	07 May 26
18	Install New Carrier Pipe - 8m	0.3d	0.7d	1	1d	07 May 26	07 May 26
19	Footway	0d	0d	0	11d	08 May 26	22 May 26
20	Excavate New Kerbline - 29.5mm	0.4d	0.6d	1	1d	08 May 26	08 May 26
21	Lay New Kerbline - 29.5m	0.4d	0.6d	1	1d	11 May 26	11 May 26
22	Regulating Sub Base - 43m2	0.5d	0.5d	1	1d	12 May 26	12 May 26
23	Lay New Tactiles - 6m2	0.5d	0.5d	1	1d	15 May 26	15 May 26
24	Lay New PCC Slabs - 43m2	1.5d	0.5d	2	2d	20 May 26	21 May 26
25	Grouting - 43m2	0.9d	0.1d	1	1d	22 May 26	22 May 26
26	Carriageway	0d	0d	0	4d	25 May 26	28 May 26
27	Lay 60mm AC20 - 12m2 Road & 9m2 Channel	0.3d	0.7d	1	1d	25 May 26	25 May 26
28	Lay 50mm HRA 35/14 - 12m2 Road & 9m2 Channel	0.3d	0.7d	1	1d	25 May 26	25 May 26
29	Road Markings	1.8d	0.2d	2	2d	27 May 26	28 May 26
30	Junction	0d	0d	0	18d	05 May 26	28 May 26
31	Downtakings	0d	0d	0	3d	05 May 26	07 May 26
32	Excavate Existing Footway - 43m2	0.8d	0.2d	1	1d	05 May 26	05 May 26
33	Excavate Existing Carriageway Setts- 30m	0.8d	0.2d	1	1d	06 May 26	06 May 26
34	Removal of Kerb 40.5m	0.5d	0.5d	1	1d	05 May 26	05 May 26
35	Removal Bollards - 13Nr	0.5d	0.5d	1	1d	07 May 26	07 May 26
36	Drainage	0d	0d	0	1d	07 May 26	07 May 26
37	Install Gully Pot & Cover - 1Nr	0.3d	0.7d	1	1d	07 May 26	07 May 26
38	Install New Carrier Pipe - 8m	0.3d	0.7d	1	1d	07 May 26	07 May 26
39	Footway	0d	0d	0	12d	08 May 26	25 May 26
40	Excavate New Kerbline - 84m & 28m HK & 26m BN	0.4d	0.6d	1	1d	08 May 26	08 May 26
41	Lay New Kerbline - 84m & 28m HK & 26m BN	0.4d	0.6d	1	1d	11 May 26	11 May 26
42	Regulating Sub Base - 57.3m2	0.4d	0.6d	1	1d	12 May 26	12 May 26
43	Install New Bollards - 22Nr	1.5d	0.5d	2	2d	13 May 26	14 May 26
44	Lay New Tactiles - 10.8m2	0.9d	0.1d	1	1d	15 May 26	15 May 26
45	Lay New PCC Slabs - 46.5m2	1.5d	0.5d	2	2d	18 May 26	19 May 26
46	Grouting - 57.3m2	0.9d	0.1d	1	1d	22 May 26	22 May 26
47	Planter Topsoil - 40m2	0.9d	0.1d	1	1d	25 May 26	25 May 26
48	Carriageway	0d	0d	0	4d	25 May 26	28 May 26
49	Cold Milling at 50mm - 280m2	0.3d	0.7d	1	1d	25 May 26	25 May 26
50	Lay 60mm AC20 Regulating Table - 53.5m2	0.3d	0.7d	1	1d	25 May 26	25 May 26
51	Lay 50mm HRA 35/14 - 280m2	0.3d	0.7d	1	1d	26 May 26	26 May 26
52	Road Markings	1.8d	0.2d	2	2d	27 May 26	28 May 26
53	**Phase 2**	**0d**	**0d**	**0**	**15d**	**01 Jun 26**	**22 Jun 26**
54	Traffic Management	0d	0d	0	0d	01 Jun 26	01 Jun 26
55	Road Closure - PH2	0d	0d	0	0d	01 Jun 26	01 Jun 26
56	Downtakings	0d	0d	0	4d	02 Jun 26	05 Jun 26
57	Excavate Existing Footway - 91.6m2	0.8d	0.2d	1	1d	02 Jun 26	02 Jun 26
58	Excavate Existing Carriageway - 79.5m2	0.8d	0.2d	1	1d	03 Jun 26	03 Jun 26
59	Removal of Kerb 37.5m	0.5d	0.5d	1	1d	04 Jun 26	04 Jun 26
60	Excavate Existing Steps - 76m	0.8d	0.2d	1	1d	05 Jun 26	05 Jun 26
61	Drainage	0d	0d	0	1d	08 Jun 26	08 Jun 26
62	Install Gully Pot & Cover - 1Nr	0.8d	0.2d	1	1d	08 Jun 26	08 Jun 26
63	Install New Carrier Pipe - 8m	0.8d	0.2d	1	1d	08 Jun 26	08 Jun 26
64	Wall & Steps	0d	0d	0	5d	08 Jun 26	12 Jun 26
65	Install New Wall - 15m	1.5d	0.5d	2	2d	08 Jun 26	09 Jun 26
66	Fix Existing Wall - TBC	0.5d	0.5d	1	1d	10 Jun 26	10 Jun 26
67	Install New Steps! - 24m	1.5d	0.5d	2	2d	11 Jun 26	12 Jun 26
68	Footway	0d	0d	0	10d	08 Jun 26	19 Jun 26
69	Excavate New Kerbline - 67.5m & 7m HK & 12m BN	0.4d	0.6d	1	1d	08 Jun 26	08 Jun 26
70	Lay New Kerbline - 84m & 28m HK & 26m BN	0.4d	0.6d	1	1d	09 Jun 26	09 Jun 26
71	Regulating Sub Base - 57.3m2	0.4d	0.6d	1	1d	10 Jun 26	10 Jun 26
72	Install New Cycle Hoops - 5Nr	0.5d	0.5d	1	1d	11 Jun 26	11 Jun 26
73	Install New Bollards - 8Nr	0.5d	0.5d	1	1d	11 Jun 26	11 Jun 26
74	Lay New Tactiles - 14.6m2	0.5d	0.5d	1	1d	15 Jun 26	15 Jun 26
75	Lay New Corduroy Slabs - 21.5m2	0.5d	0.5d	1	1d	15 Jun 26	15 Jun 26
76	Lay New PCC Slabs - 52.5m2	1.8d	0.2d	2	2d	16 Jun 26	17 Jun 26
77	Grouting - 52.5m2	0.9d	0.1d	1	1d	18 Jun 26	18 Jun 26
78	Planter Topsoil - 48.5m2	0.9d	0.1d	1	1d	19 Jun 26	19 Jun 26
79	Lay 50mm 20mm DBM - 3.5m2	0.2d	0.8d	1	1d	19 Jun 26	19 Jun 26
80	Lay 30mm 10/10 HRA - 3.5m2	0.2d	0.8d	1	1d	19 Jun 26	19 Jun 26
81	Carriageway	0d	0d	0	2d	19 Jun 26	22 Jun 26
82	Cold Milling at 50mm - 82.5m2	0.2d	0.8d	1	1d	19 Jun 26	19 Jun 26
83	Lay 60mm AC20 Regulating Table - 32.5m2	0.2d	0.8d	1	1d	19 Jun 26	19 Jun 26
84	Lay 50mm HRA 35/14 - 82.5m2 & 7.5m2 Channel	0.2d	0.8d	1	1d	19 Jun 26	19 Jun 26
85	Road Markings	0.8d	0.2d	1	1d	22 Jun 26	22 Jun 26
86	**Phase 3**	**0d**	**0d**	**0**	**4d**	**22 Jun 26**	**26 Jun 26**
87	Traffic Management	0d	0d	0	0d	22 Jun 26	22 Jun 26
88	Road Closure - PH3	0d	0d	0	0d	22 Jun 26	22 Jun 26
89	Downtakings	0d	0d	0	1d	23 Jun 26	23 Jun 26
90	Excavate Existing Footway - 13.6m2	0.8d	0.2d	1	1d	23 Jun 26	23 Jun 26
91	Removal of Kerb 7m	0.5d	0.5d	1	1d	23 Jun 26	23 Jun 26
92	Footway	0d	0d	0	4d	23 Jun 26	26 Jun 26
93	Excavate New Kerbline - 7m	0.4d	0.6d	1	1d	23 Jun 26	23 Jun 26
94	Lay New Kerbline - 7m	0.4d	0.6d	1	1d	23 Jun 26	23 Jun 26
95	Regulating Sub Base - 14.5m2	0.2d	0.8d	1	1d	24 Jun 26	24 Jun 26
96	Install New Cycle Hoops - 3Nr	0.5d	0.5d	1	1d	24 Jun 26	24 Jun 26
97	Lay New Tactiles - 5.5m2	0.5d	0.5d	1	1d	25 Jun 26	25 Jun 26
98	Lay New PCC Slabs - 9m2	0.5d	0.5d	1	1d	25 Jun 26	25 Jun 26
99	Grouting - 14.5m2	0.25d	0.75d	1	1d	26 Jun 26	26 Jun 26
100	Carriageway	0d	0d	0	2d	24 Jun 26	25 Jun 26
101	Lay 50mm HRA 35/14 - 3m2 Channel	0.2d	0.8d	1	1d	24 Jun 26	24 Jun 26
102	Road Markings	0.2d	0.8d	1	1d	25 Jun 26	25 Jun 26
103	**Planned Completion**	**0d**	**0d**	**0**	**0d**	**26 Jun 26**	**26 Jun 26**
104	**Completion Date**	**0d**	**0d**	**0**	**0d**	**21 Aug 26**	**21 Aug 26**

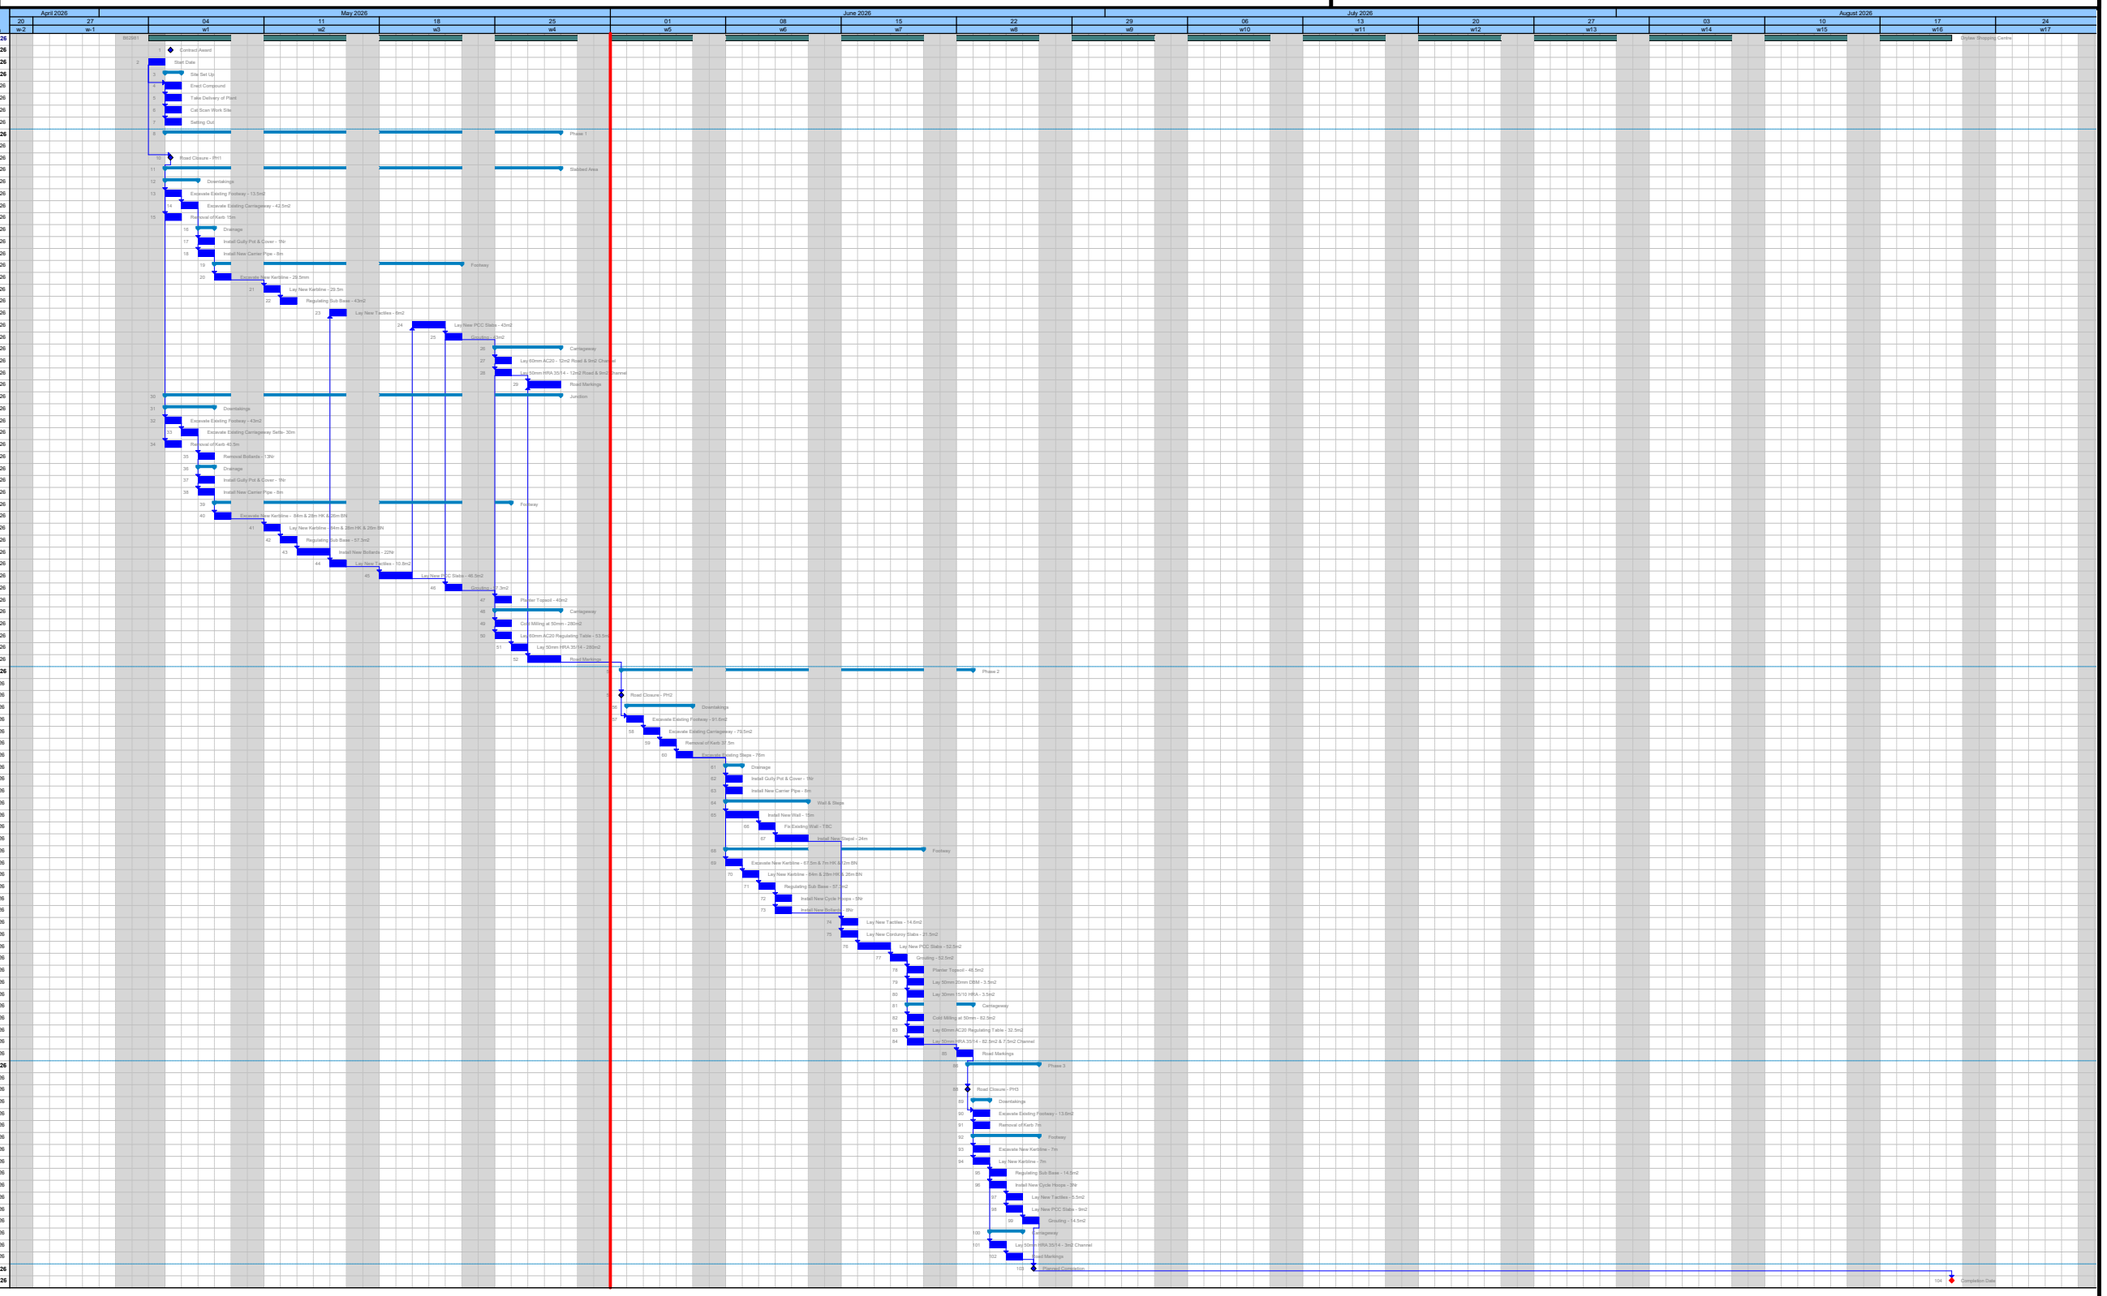

General Comments: Proposed Programme	**Author:** H.Granger	**Programme No.**	**Revision**	**Page**
Revision Comments:	**Date Drawn:**	B62981	B	1
